


ID	Calendar Days	Task Name	Duration	% Complete	Start	Finish
0	298 days	39008 - Davie County Park	205 days	52%	Mon 3/4/19	Thu 12/26/19
2	1 days	Owner Awarded Part F Grant Money	1 day	0%	Fri 11/1/19	Fri 11/1/19
38	49 days	BUILDING EXTERIOR	34 days	0%	Wed 10/2/19	Tue 11/19/19
39	14 days	Roof Fascia & Gutters	10 days	0%	Wed 10/2/19	Tue 10/15/19
40	5 days	Footings for Front Columns	3 days	0%	Thu 10/10/19	Mon 10/14/19
41	7 days	Brick Columns	5 days	0%	Tue 10/15/19	Mon 10/21/19
42	7 days	Electrical in Columns	5 days	0%	Tue 10/15/19	Mon 10/21/19
43	7 days	Brick Wainscot	5 days	0%	Tue 10/22/19	Mon 10/28/19
44	3 days	Pour Sidewalks at Front Entry	3 days	0%	Tue 10/29/19	Thu 10/31/19
45	7 days	Install New Storefront Doors & Hardware	5 days	0%	Fri 11/1/19	Thu 11/7/19
46	8 days	ADA Devices	5 days	0%	Fri 11/8/19	Fri 11/15/19
47	3 days	Set Steel at Front Entry	3 days	0%	Tue 11/12/19	Thu 11/14/19
48	1 days	Install Signage Panel	1 day	0%	Fri 11/15/19	Fri 11/15/19
49	2 days	Light Fixtures	2 days	0%	Mon 11/18/19	Tue 11/19/19
50	73 days	BUILDING INTERIOR	50 days	3%	Mon 10/7/19	Wed 12/18/19
51	19 days	Prime & 1st Finish Coat everthing minus Gym	15 days	27%	Mon 10/7/19	Fri 10/25/19
52	1 days	Field Measure for Countertops	1 day	0%	Mon 10/14/19	Mon 10/14/19
53	21 days	Leadtime for Countertops	15 days	0%	Tue 10/15/19	Mon 11/4/19
54	5 days	Ceiling Grid	5 days	0%	Mon 10/21/19	Fri 10/25/19
55	12 days	Light Fixtures	10 days	0%	Mon 10/28/19	Fri 11/8/19
56	12 days	HVAC Grilles	10 days	0%	Mon 10/28/19	Fri 11/8/19
57	12 days	Toilet Partitions	10 days	0%	Mon 10/28/19	Fri 11/8/19
58	1 days	Install Counter Tops	1 day	0%	Tue 11/5/19	Tue 11/5/19
59	8 days	Remaining Plumbing Fixtures	5 days	0%	Wed 11/6/19	Wed 11/13/19
60	7 days	Toilet Accessories	5 days	0%	Tue 11/12/19	Mon 11/18/19
61	7 days	Ceiling Tile	5 days	0%	Tue 11/12/19	Mon 11/18/19
62	14 days	HVAC Test & Balance	10 days	0%	Tue 11/12/19	Mon 11/25/19
63	16 days	Frames, Doors, and Hardware	10 days	0%	Tue 11/19/19	Wed 12/4/19
64	16 days	Finish Coat of Paint	10 days	0%	Tue 11/19/19	Wed 12/4/19
65	5 days	Signage	3 days	0%	Thu 12/5/19	Mon 12/9/19
66	7 days	Carpet & Base	5 days	0%	Thu 12/5/19	Wed 12/11/19

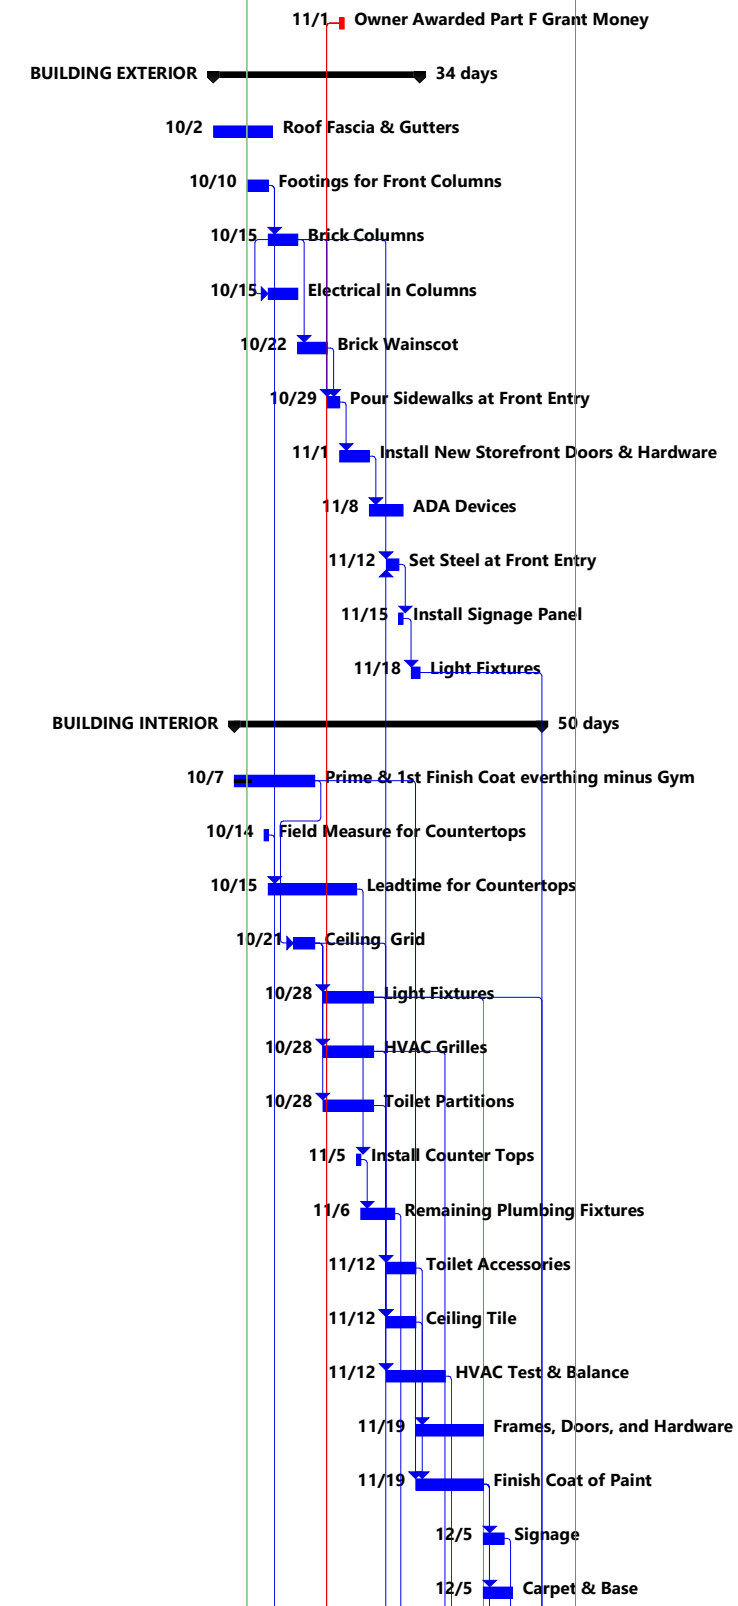

Project: 39008 - Davie County P
Date: Thu 10/10/19

Task Milestone Project Summary Deadline Baseline Baseline Summary

Split Summary Group By Summary Critical Task Baseline Milestone Progress

ID	Calendar Days	Task Name	Duration	% Complete	Start	Finish	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March
67	7 days	Paint Gym	5 days	0%	Thu 12/5/19	Wed 12/11/19															
68	7 days	Fire Alarm Devices	5 days	0%	Thu 12/5/19	Wed 12/11/19															
69	14 days	Electrical Devices	10 days	0%	Thu 12/5/19	Wed 12/18/19															
70	7 days	Re-Finish Hardwood Floors in	5 days	0%	Thu 12/12/19	Wed 12/18/19															
71	19 days	FOOTBALL STADIUM ELECTRICAL RE-WORK	14 days	0%	Mon 11/4/19	Fri 11/22/19															
72	2 days	Form & Prep Transformer Pad	2 days	0%	Mon 11/4/19	Tue 11/5/19															
73	1 days	Energy United Inspection of Pads	1 day	0%	Wed 11/6/19	Wed 11/6/19															
74	1 days	Pour Transformer Pads	1 day	0%	Thu 11/7/19	Thu 11/7/19															
75	12 days	New Underground Electrical & Panels	7 days	0%	Fri 11/8/19	Tue 11/19/19															
76	3 days	Energy United Conversion to New Electrical	3 days	0%	Wed 11/20/19	Fri 11/22/19															
77	289 days	SITework ON PARK SIDE	200 days	60%	Mon 3/4/19	Tue 12/17/19															
90	3 days	Monument Sign Footing	3 days	0%	Tue 10/15/19	Thu 10/17/19															
91	7 days	Monument Sign Base	5 days	0%	Fri 10/18/19	Thu 10/24/19															
92	5 days	Seed outside areas of ballfields	5 days	0%	Mon 10/28/19	Fri 11/1/19															
93	1 days	DENR acceptance to fill in sediment pond	1 day	0%	Mon 11/4/19	Mon 11/4/19															
94	3 days	Grade for Trails	3 days	0%	Tue 11/5/19	Thu 11/7/19															
95	8 days	Aggregate Trail between Ballfields	5 days	0%	Fri 11/8/19	Fri 11/15/19															
96	5 days	Asphalt Paving from Dog Park to Nature Trail	5 days	0%	Mon 11/18/19	Fri 11/22/19															
97	9 days	Site Furnishings	5 days	0%	Mon 11/25/19	Tue 12/3/19															
98	23 days	Landscaping	15 days	0%	Mon 11/25/19	Tue 12/17/19															
99	3 days	Install Digital Sign & Letters on Monument Sign	3 days	0%	Tue 12/10/19	Thu 12/12/19															
100	1 days	Wayfinding Signage	1 day	0%	Fri 12/13/19	Fri 12/13/19															
101	187 days	SPLASH PAD	130 days	61%	Mon 6/3/19	Fri 12/6/19															
105	57 days	Underground Plumbing to Features	40 days	93%	Tue 8/20/19	Tue 10/15/19															
106	7 days	Backfill	5 days	0%	Wed 10/16/19	Tue 10/22/19															
107	7 days	Form & Pour Wet Slab	5 days	0%	Wed 10/23/19	Tue 10/29/19															
108	7 days	Form & Pour Spray Free Area	5 days	0%	Wed 10/30/19	Tue 11/5/19															
109	15 days	Set Features of Splash Pad & Hook Up	10 days	0%	Wed 10/30/19	Wed 11/13/19															
110	14 days	Hookup Equipment in Pump Room	10 days	0%	Thu 11/14/19	Wed 11/27/19															
111	5 days	Startup & Chemical Balancing	5 days	0%	Mon 12/2/19	Fri 12/6/19															
112	7 days	Perimeter Fencing	5 days	0%	Thu 11/14/19	Wed 11/20/19															

Project: 39008 - Davie County Park
 Date: Thu 10/10/19


Task Milestone Project Summary Deadline Baseline Baseline Summary
Split Summary Group By Summary Critical Task Baseline Milestone Progress

ID	Calendar Days	Task Name	Duration	% Complete	Start	Finish	January	February	March	April	May	June	July	August	September	October	November	December	January	February	March
113	16 days	Landscaping	10 days	0%	Thu 11/21/19	Fri 12/6/19											11/21				
114	75 days	AMPHITHEATER	54 days	68%	Mon 7/8/19	Fri 9/20/19															
122	7 days	Prep & Pour Slab	5 days	60%	Tue 10/8/19	Mon 10/14/19											10/8				
123	5 days	Set Steel	5 days	0%	Mon 11/4/19	Fri 11/8/19											11/4				
124	10 days	Set Wood Nailers, Decking Boards & Felt	8 days	0%	Tue 11/12/19	Thu 11/21/19											11/12				
125	4 days	Shingles	2 days	0%	Fri 11/22/19	Mon 11/25/19											11/22				
126	11 days	Conduit & Wiring	5 days	0%	Fri 11/22/19	Mon 12/2/19											11/22				
127	7 days	Set Electrical Gear	5 days	0%	Tue 12/3/19	Mon 12/9/19											12/3				
128	2 days	Prime & 1st Finish Coat	2 days	0%	Tue 12/10/19	Wed 12/11/19											12/10				
129	7 days	Set Light Fixtures	5 days	0%	Thu 12/12/19	Wed 12/18/19											12/12				
130	2 days	Finish Coat of Paint	2 days	0%	Thu 12/19/19	Fri 12/20/19											12/19				
131	107 days	NATURE TRAIL	76 days	79%	Mon 7/8/19	Tue 10/22/19															
136	5 days	Fine Grade & Stone Trails	5 days	80%	Mon 10/7/19	Fri 10/11/19											10/7				
137	2 days	Asphalt Paving	2 days	0%	Mon 10/14/19	Tue 10/15/19											10/14				
138	7 days	Seeding/Landscaping	5 days	0%	Wed 10/16/19	Tue 10/22/19											10/16				
139	109 days	310' SOFTBALL/BASEBALL FIELD	75 days	43%	Fri 8/2/19	Mon 11/18/19															
146	3 days	Dugout Fence Post	3 days	0%	Mon 10/14/19	Wed 10/16/19											10/14				
147	2 days	Prep & Pour Concrete Pads at Dugouts	2 days	0%	Thu 10/17/19	Fri 10/18/19											10/17				
148	7 days	Chainlink on Fence Post & Gates	5 days	0%	Thu 10/17/19	Wed 10/23/19											10/17				
149	3 days	Trench Drain at Backstop	3 days	0%	Mon 10/21/19	Wed 10/23/19											10/21				
150	5 days	Frame Dugout Roofs	5 days	0%	Mon 10/21/19	Fri 10/25/19											10/21				
151	1 days	Shingle Dugout Roofs	1 day	0%	Mon 10/28/19	Mon 10/28/19											10/28				
152	5 days	Install Well Pump	5 days	0%	Mon 10/28/19	Fri 11/1/19											10/28				
153	5 days	Prep & Temporary Seed Outfield	5 days	0%	Mon 10/28/19	Fri 11/1/19											10/28				
154	7 days	Sidewalks Around Ballfield	5 days	0%	Thu 10/24/19	Wed 10/30/19											10/24				
155	1 days	Bleachers	1 day	0%	Mon 11/18/19	Mon 11/18/19											11/18				
156	1 days	Install Bases, Pitching Rubber & Home Plate	1 day	0%	Mon 11/18/19	Mon 11/18/19											11/18				
157	66 days	FRONT PARKING LOT	45 days	20%	Mon 9/30/19	Wed 12/4/19															
160	7 days	Grade & Proof Roll Subgrade in New Paving Areas	5 days	20%	Thu 10/10/19	Wed 10/16/19											10/10				
161	14 days	Curb & Gutter	10 days	0%	Thu 10/17/19	Wed 10/30/19											10/17				
162	7 days	Sidewalks Around Building & Bollards	5 days	0%	Thu 10/31/19	Wed 11/6/19											10/31				

Project: 39008 - Davie County Park
 Date: Thu 10/10/19

Task Milestone Project Summary Deadline Baseline Baseline Summary
Split Summary Group By Summary Critical Task Baseline Milestone Progress

ID	Calendar Days	Task Name	Duration	% Complete	Start	Finish
163	8 days	Stone Base & Setup	5 days	0%	Thu 11/7/19	Thu 11/14/19
164	5 days	Asphalt Paving	3 days	0%	Fri 11/15/19	Tue 11/19/19
165	7 days	Landscaping in Islands & Around Building	5 days	0%	Wed 11/20/19	Tue 11/26/19
166	6 days	Seal Coat Areas to Remain	2 days	0%	Wed 11/27/19	Mon 12/2/19
167	2 days	Striping & Handicap Signage	2 days	0%	Tue 12/3/19	Wed 12/4/19
168	72 days	200' FUTURE SOFTBALL/BASEBALL FIELD	51 days	55%	Thu 8/29/19	Fri 11/8/19
171	5 days	Seeding/Landscaping	5 days	0%	Mon 11/4/19	Fri 11/8/19
172	110 days	CIVIC GREEN	74 days	25%	Thu 8/29/19	Mon 12/16/19
176	7 days	Irrigation System	5 days	20%	Thu 10/10/19	Wed 10/16/19
177	6 days	Fine Grade	4 days	0%	Thu 10/17/19	Tue 10/22/19
178	9 days	Remaining Sidewalks	5 days	0%	Tue 11/26/19	Wed 12/4/19
179	5 days	Aggregate Behind Amphitheater	3 days	0%	Thu 12/5/19	Mon 12/9/19
180	7 days	Sod Civic Green	5 days	0%	Thu 12/5/19	Wed 12/11/19
181	5 days	Landscaping Around Ampitheater	3 days	0%	Thu 12/12/19	Mon 12/16/19
182	15 days	SHELTER AT CIVIC GREEN	10 days	0%	Fri 11/1/19	Fri 11/15/19
183	1 days	Layout	1 day	0%	Fri 11/1/19	Fri 11/1/19
184	2 days	Footings	2 days	0%	Mon 11/4/19	Tue 11/5/19
185	2 days	Prep & Pour Slab	2 days	0%	Wed 11/6/19	Thu 11/7/19
186	8 days	Structure	5 days	0%	Fri 11/8/19	Fri 11/15/19
187	15 days	BOCCE & HORSESHOE AREA	10 days	0%	Fri 11/1/19	Fri 11/15/19
188	1 days	Layout	1 day	0%	Fri 11/1/19	Fri 11/1/19
189	4 days	Form & Pour Perimeter Curb	4 days	0%	Mon 11/4/19	Thu 11/7/19
190	1 days	Set Horseshoe Pins/Backstops & Bocce Score Board Post	1 day	0%	Fri 11/8/19	Fri 11/8/19
191	5 days	Prep & Pour Concrete Base to Drain @ Bocce	2 days	0%	Fri 11/8/19	Tue 11/12/19
192	2 days	Filter Fabric, Stone, and Sand	2 days	0%	Wed 11/13/19	Thu 11/14/19
193	1 days	Install Rubber Bumpers & Other Misc Items	1 day	0%	Fri 11/15/19	Fri 11/15/19
194	33 days	DOG PARKS	20 days	0%	Fri 11/1/19	Tue 12/3/19
195	4 days	Prep & Pour Concrete Pads at Entry Ways	2 days	0%	Fri 11/1/19	Mon 11/4/19
196	1 days	Set Water Fountains	1 day	0%	Fri 11/8/19	Fri 11/8/19
197	8 days	Fencing	5 days	0%	Tue 11/5/19	Tue 11/12/19
198	7 days	Landscaping In & Around Dog Park	5 days	0%	Wed 11/13/19	Tue 11/19/19

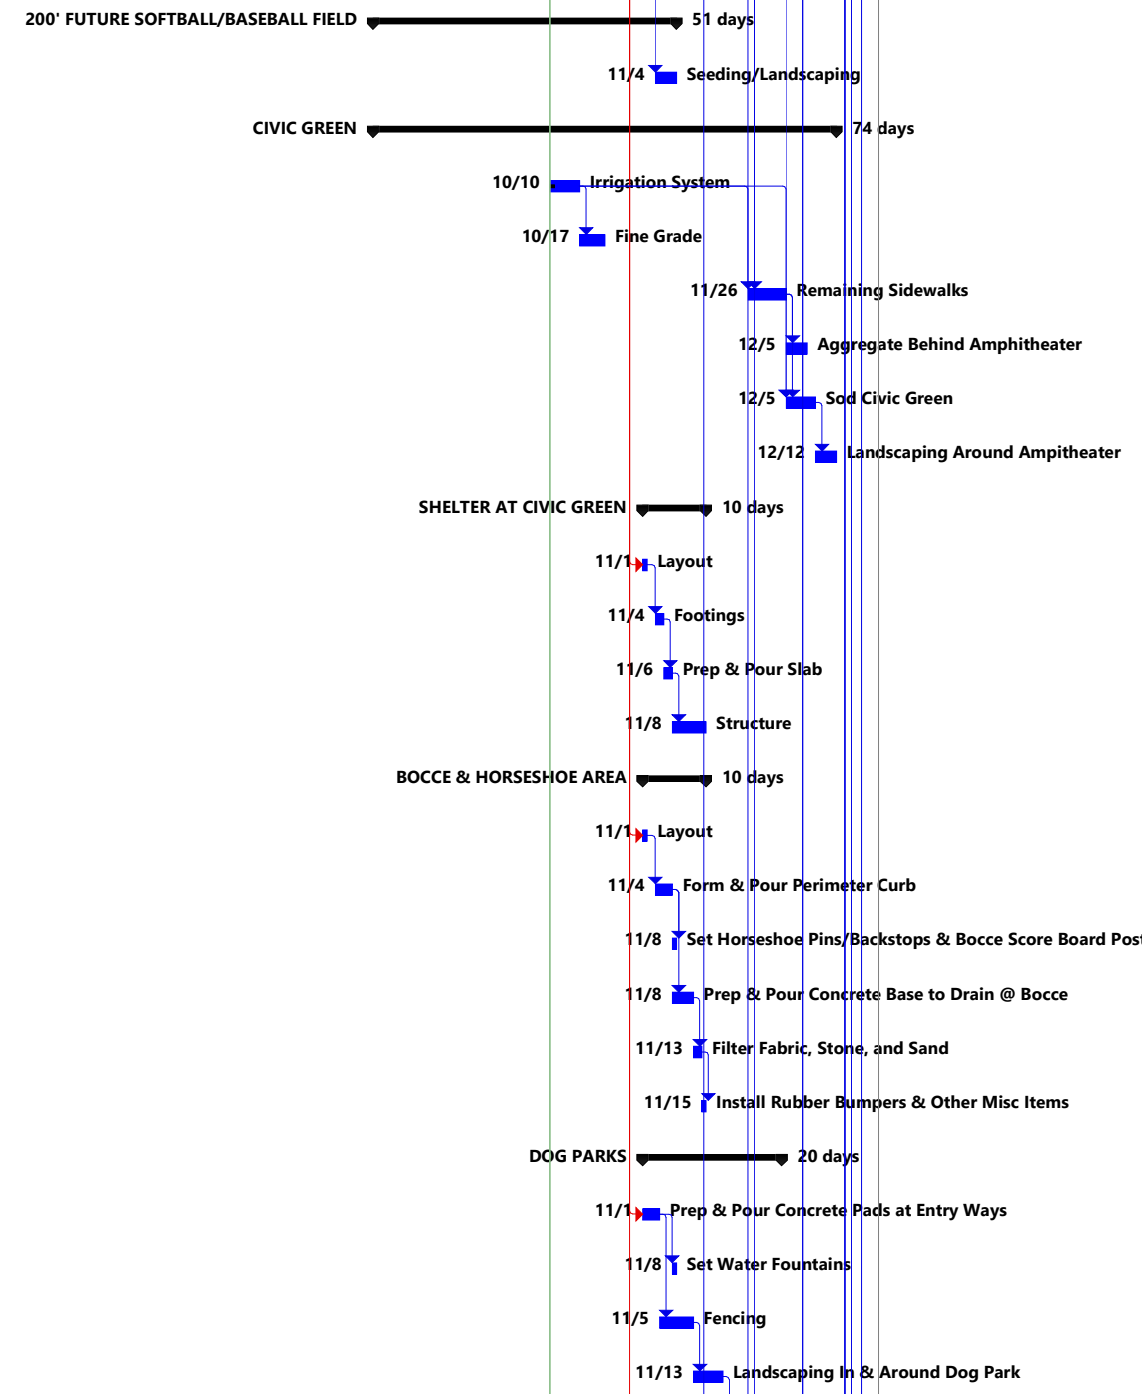


Project: 39008 - Davie County P
Date: Thu 10/10/19

Task: [Blue bar] Milestone: [Diamond] Project Summary: [Grey bar] Deadline: [Green triangle] Baseline: [Grey bar] Baseline Summary: [Grey bar]

Split: [Dotted line] Summary: [Black bar] Group By Summary: [Black bar] Critical Task: [Red bar] Baseline Milestone: [Diamond] Progress: [Black bar]

ID	Calendar Days	Task Name	Duration	% Complete	Start	Finish
199	3 days	Aggregate Fines Path	3 days	0%	Wed 11/20/19	Fri 11/22/19
200	9 days	HD Asphalt Path	5 days	0%	Mon 11/25/19	Tue 12/3/19
201	56 days	PLAYGROUND	35 days	0%	Fri 11/1/19	Thu 12/26/19
202	4 days	Survey Points & Layout	2 days	0%	Fri 11/1/19	Mon 11/4/19
203	8 days	Pour Footings	5 days	0%	Tue 11/5/19	Tue 11/12/19
204	14 days	Set Playground Features	10 days	0%	Wed 11/13/19	Tue 11/26/19
205	7 days	Set Shade Structures	3 days	0%	Wed 11/27/19	Tue 12/3/19
206	3 days	Underground Drainage	3 days	0%	Wed 12/4/19	Fri 12/6/19
207	2 days	Perimeter Border	2 days	0%	Mon 12/9/19	Tue 12/10/19
208	16 days	Play Surface	10 days	0%	Wed 12/11/19	Thu 12/26/19
209	40 days	FINAL INSPECTIONS	26 days	0%	Thu 11/14/19	Mon 12/23/19
210	1 days	Plumbing	1 day	0%	Thu 11/14/19	Thu 11/14/19
211	1 days	HVAC	1 day	0%	Tue 11/26/19	Tue 11/26/19
212	1 days	Health Department	1 day	0%	Mon 12/9/19	Mon 12/9/19
213	1 days	Electrical	1 day	0%	Thu 12/19/19	Thu 12/19/19
214	1 days	Building	1 day	0%	Fri 12/20/19	Fri 12/20/19
215	1 days	Fire Marshall	1 day	0%	Mon 12/23/19	Mon 12/23/19

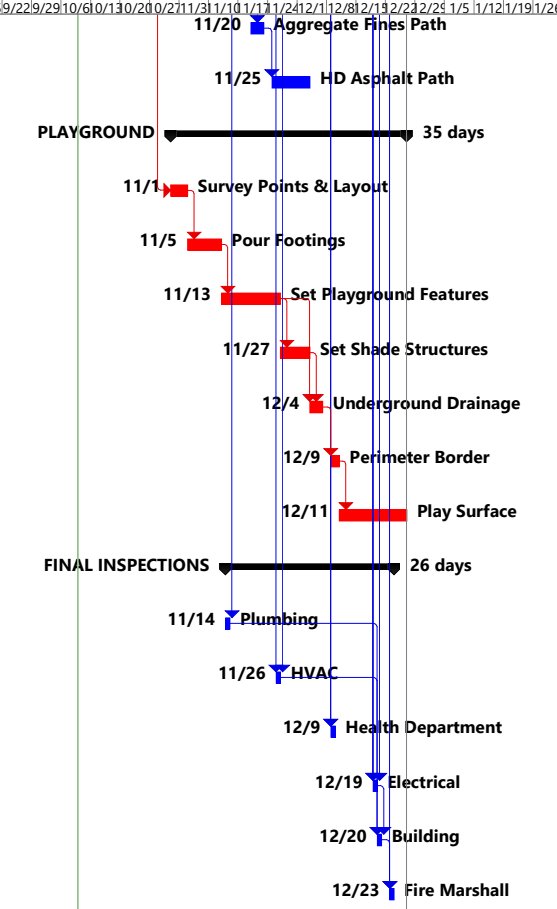

Project: 39008 - Davie County P
Date: Thu 10/10/19

Task: [Blue Bar] Milestone: [Diamond] Project Summary: [Grey Bar] Deadline: [Green Triangle] Baseline: [Grey Bar] Baseline Summary: [Grey Bar]

Split: [Dotted Line] Summary: [Black Arrow] Group By Summary: [Black Arrow] Critical Task: [Red Bar] Baseline Milestone: [Diamond] Progress: [Black Arrow]
